Procureline
PROCUREMENT SYSTEM

PROCUREMENT SYSTEM

Rollout Plan

How Procureline goes live across the group's fifteen business units: the infrastructure gate, a two-unit pilot, two Zimbabwe waves and South Africa, starting Monday 16 November 2026.

ONLINE AT

www.procureline.co.zw

Sign in, register as a supplier, or read more about Procureline.

WEBSITE	STARTS	STATUS
www.procureline.co.zw	Monday 16 November 2026	Draft for review · 6 November 2026

PROCURELINE ROLLOUT PLAN

Contents

	At a glance	**3**
PART 1	**How it works**	**4**
	1.1 One address per business unit	4
	1.2 Launch order	4
	1.3 Built-in controls	5
PART 2	**Where it stands**	**6**
	2.1 Live today	6
	2.2 The infrastructure gate: 16 to 27 November	6
PART 3	**What the system does**	**8**
	3.1 Signing in	8
	3.2 Dashboards	8
	3.3 Requisitions	9
	3.4 Quotations and awards	9
	3.5 Stores	10
	3.6 Invoices, payments and budgets	10
	3.7 Suppliers	11
	3.8 Administration and audit	11
PART 4	**Rollout plan**	**12**
	4.1 Phases and dates	12
	4.2 One week of set-up, for every unit	13
	4.3 Pilot exit tests	13
	4.4 Main risks	14
	4.5 Launch schedule	15

SUMMARY

At a glance

Procureline is the group's procurement system. Each business unit has its own address and its own private data, with the group's procurement rules built in. This plan says in what order the fifteen units go live and on which dates, starting **Monday 16 November 2026**.

15
Business units, each at its own address

7 Dec
Pilot units live: Fossil Contracting and Dokuma

1 Mar
Every Zimbabwe unit live, 2027

18
Weeks from the start to the last unit

Product	Procureline, a procurement and stores system used in a web browser, at **www.procureline.co.zw**
Unit address	Its own subdomain, for example **fossil.procureline.co.zw**, and its own database that no other unit can see
Start	**Monday 16 November 2026:** two weeks of infrastructure work, signed off on Friday 27 November
Pilot	Fossil Contracting and Dokuma, set up from 30 November, live on real purchases from **Monday 7 December**
Then	Khayah Cement, Titan and Kurima Centre on **25 January 2027**; seven more Zimbabwe units two a week through February, the last on **1 March**; South Africa on **15 March**, provisionally
Festive period	21 December to 1 January: the pilot units keep buying through Procureline; nothing else is set up or goes live
Decisions	Gate signed off 27 November; go decision after the pilot on **15 January 2027**; the 5 March review confirms South Africa
Done when	Every unit raises its requisitions in Procureline and has closed its old process after the one-month fallback

Reading the dates. Weeks run Monday to Friday; W1 is 16 to 20 November 2026. A unit spends one week on set-up and training, goes live on the following Monday and stays live, with its old process as a fallback for one month. Provisional dates are confirmed at the review on 5 March 2027. How a unit is set up is in the **Launch Manual**; how each role works is in the **User Manual**.

PART 1

How it works

Every business unit runs on the same system and is kept completely separate from the others. The order of go-lives is chosen so that each wave proves something the next one depends on.

1.1 One address per business unit

ITEM	HOW IT WORKS
Address	A subdomain of procureline.co.zw, for example **fossil.procureline.co.zw**. All fifteen addresses already answer over HTTPS
Sign-in	The address identifies the unit, so users never choose one. Email and password, then a six-digit code sent by email
Data	Each unit has its own database. A script check proves that no unit can see another's records
Rules	The approval chain, the COO limit, the exchange rate and the supplier document rules are set per unit, so a unit's own delegation of authority is what the system enforces
Suppliers	Suppliers register and quote through the unit's own address. A supplier that serves two units registers with each

1.2 Launch order

PHASE	BUSINESS UNITS	WHY IN THIS ORDER
0. Infrastructure gate	All	Nothing goes live on test accounts. Backups, real email and two-factor sign-in come first
1. Pilot	Fossil Contracting, Dokuma	The units the system was built with. Real purchases over the festive period prove it before anyone else depends on it
2. Second wave	Khayah Cement, Titan, Kurima Centre	Cement, services and retail: three different kinds of buying, three weeks after the go decision
3. Third wave	Mandfar, Masimba, Persimmon, ProPlastics, Rhopower, The Grain Hub, Trends	Two units a week, each after its own rehearsal purchase, once set-up has become routine
4. South Africa	Enviro Plastic, Mangethe, Thando Kinetics	Rand pricing and South African supplier documents are prepared during the third wave and confirmed at its review

1.3 Built-in controls

These apply in every unit from the day it goes live. They are the procurement procedure, enforced by the system rather than by memory.

CONTROL	WHAT IT MEANS
Three quotations	Fewer than three needs a recorded waiver with a reason, approved by the COO
Approvals	Every purchase order is approved by the Head of Procurement, then Finance, and above the unit's limit (USD 5,000 unless set otherwise) by the COO
Three-way match	No invoice is approved unless the order, the goods received and the invoice agree
Activated suppliers	Only a supplier with complete documents, checked by Procurement and approved by a second person, can be awarded work
Separate units	Each unit's data is kept apart, and a session from one address is refused at another
Audit log	Every action is recorded with who did it and when, and cannot be edited

PART 2

Where it stands

The software is finished and deployed. What remains before live use is set-up, not development: the infrastructure gate below, done in the first two weeks of the plan and signed off on Friday 27 November 2026.

2.1 Live today

ITEM	STATUS ON 6 NOVEMBER 2026
Deployment	Live. All fifteen business units answer over HTTPS at their own addresses
End-to-end proof	The full purchase cycle ran against the live system on 26 October 2026 with no failures. The scripted cycle now also covers two-person supplier activation and is re-run in the gate
Data separation	Units cannot see each other's data; a script check proves it
Documents	The Launch Manual and the User Manual, version 1.0 of 6 November 2026, with screenshots of the released system
Accounts	Fossil Contracting is loaded. The other fourteen units exist as empty units waiting for their set-up week

2.2 The infrastructure gate: 16 to 27 November

Nothing goes live until every item is done and the gate is signed off by the technical lead and the rollout lead. Until two-factor sign-in is on, anyone who knows an email address and password can act as that person, Finance included. That is acceptable for testing and not for live purchasing. The detail of each item is in the Launch Manual, 1.2.

#	TASK	OWNER	DONE WHEN	WEEK
1	The group owns its domain, database account, hosting account and email-sending account, each with two administrators. Nothing is on a personal account	IT, technical team	Each account is held by the group and has two administrators	W1
2	Daily database backups with a copy kept elsewhere, and a restore performed into a scratch environment and timed	Technical team	A restore has actually been done, not only configured	W1–W2
3	Real email sending switched on, with the address used in email links correct for every unit	Technical team	A notification email links to a working page	W1

#	TASK	OWNER	DONE WHEN	WEEK
4	Two-factor sign-in on: a real six-digit code required by email	Technical team	Sign-in cannot complete without the emailed code	W1
5	The hourly alert jobs scheduled on the hosted API, for every unit	Technical team	The audit log shows the jobs running each hour	W2
6	Suppliers imported from the older register have their permanent supplier codes	Technical team	Every supplier shows a code such as `FOSSIL-SUP-00001`	W2
7	A separate test environment, so testing never touches live data	Technical team	Testers sign in somewhere other than a live address	W2
8	The scripted full cycle re-run on the live system, including two-person supplier activation	Technical team	Every step passes; the result is filed with the sign-off	W2

Exit test, Friday 27 November. An administrator signs out, requests a password reset, receives the email, sets a new password, and signs back in with a real emailed code, at a unit's own address. Then the gate is signed off and the pilot set-up starts on Monday.

If the gate slips, the pilot slips. Every week lost here moves the whole schedule by a week. Nobody goes live on the test set-up to make up time.

PART 3

What the system does

A short tour of the released system, so the reader of this plan knows what each unit is being given. The User Manual covers every screen step by step.

3.1 Signing in

Each unit signs in at its own address with email, password and a six-digit code sent by email. Suppliers register themselves through the same address.

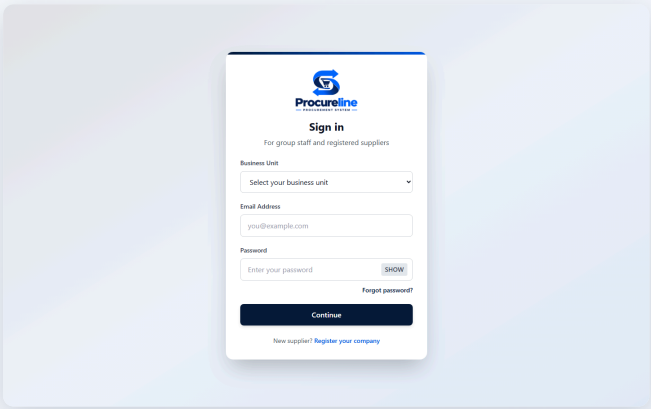


Figure The sign-in page at a unit's own address

3.2 Dashboards

Each role sees its own work: Procurement sees sourcing in progress, Finance sees what awaits approval, staff see their own requests and notifications.

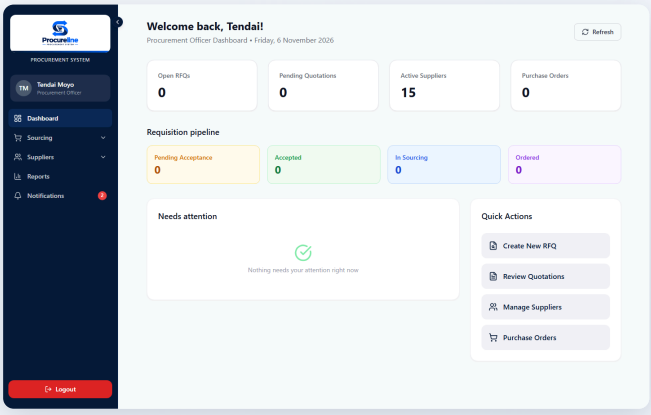


Figure A procurement officer's dashboard: the pipeline from pending acceptance to ordered

3.3 Requisitions

Any member of staff raises a requisition. The department head approves it against the budget, Stores checks whether the items are in stock, and Procurement takes the rest forward.

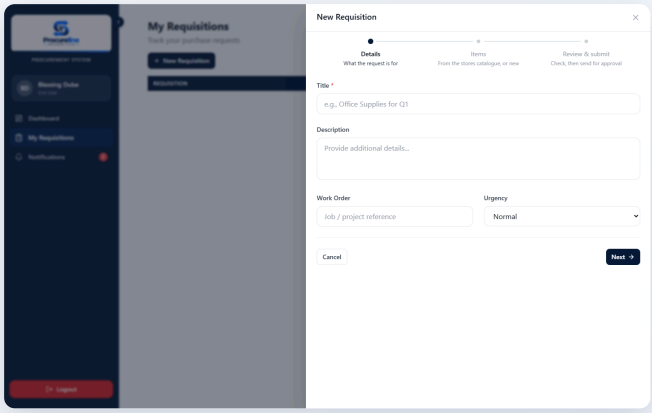


Figure Raising a requisition

3.4 Quotations and awards

Procurement publishes a request for quotation to activated suppliers, who respond online. Quotations are compared side by side; the award is authorised by the Head of Procurement, and fewer than three quotations needs a waiver.

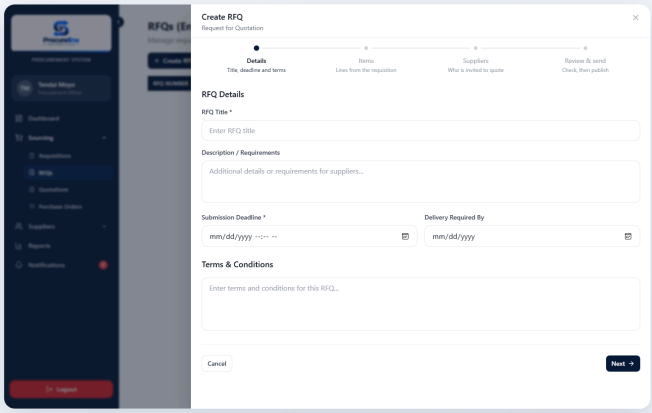


Figure Creating a request for quotation

3.5 Stores

Stores issues from stock where it can, records each delivery against the order, accepts or rejects it, and tracks stock across sites.

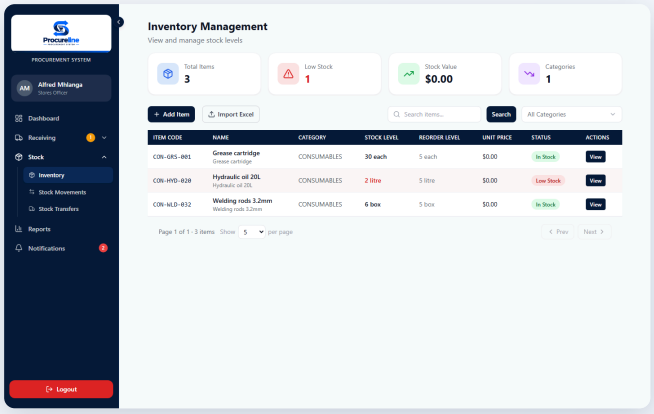


Figure Stock on hand, with reorder levels

3.6 Invoices, payments and budgets

An invoice is paid only when it matches the order and the goods received. Spending is tracked against each department's annual budget as it is committed and as it is paid.

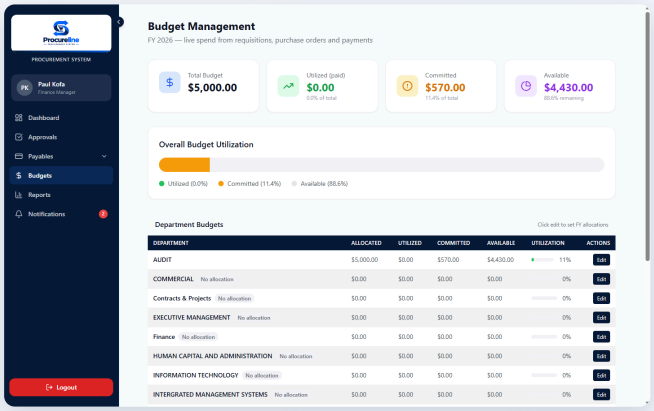


Figure Department budgets: allocated, committed, paid and available

3.7 Suppliers

A supplier uploads its compliance documents through its own portal. Procurement checks them and a second person, the Head of Procurement or the COO, approves the activation. Expired documents block an award by themselves.

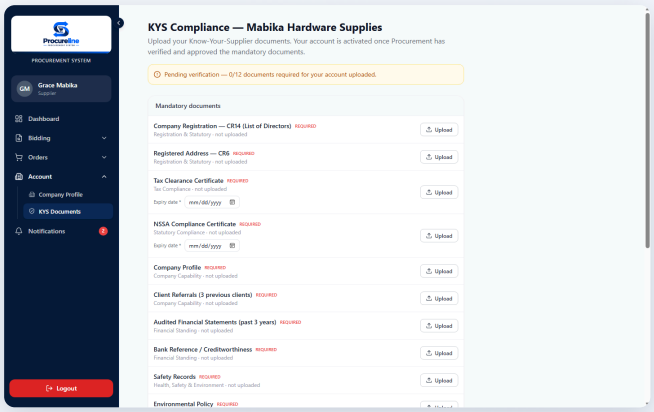


Figure A supplier's compliance documents, seen from the supplier portal

3.8 Administration and audit

Each unit's administrator manages users, departments, sites and the approval limit. Every important action is logged with who did it and when.

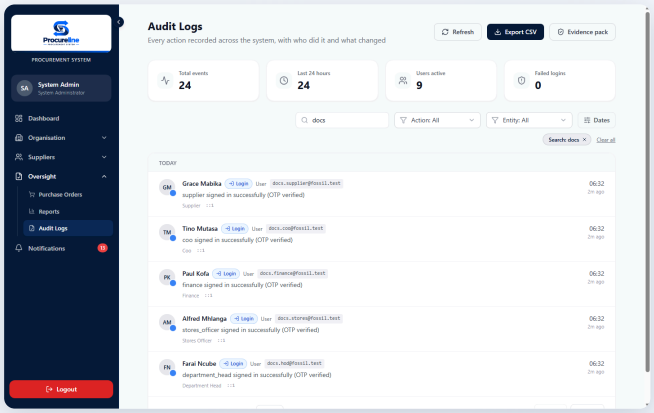


Figure The audit log

PART 4

Rollout plan

Five phases from Monday 16 November 2026. Each phase finishes with a decision that is written down before the next begins: proceed, fix first, or stop.

4.1 Phases and dates

PHASE	DATES	WEEKS	BUSINESS UNITS	WHAT HAPPENS
0. Infrastructure gate	16–27 Nov 2026	W1–W2	All	The eight items in 2.2. Exit test and sign-off on Friday 27 November
1. Pilot	30 Nov 2026 – 15 Jan 2027	W3–W9	Fossil Contracting, Dokuma	Set up and train 30 November to 4 December. **Live Monday 7 December.** Festive period 21 December to 1 January. Exit tests assessed 4 to 8 January. Review and **go decision Friday 15 January**
2. Second wave	18–29 Jan 2027	W10–W11	Khayah Cement, Titan, Kurima Centre	Set up and train 18 to 22 January. **Live Monday 25 January**
3. Third wave	1 Feb – 5 Mar 2027	W12–W16	Mandfar, Masimba, Persimmon, ProPlastics, Rhopower, The Grain Hub, Trends	Two units a week. Live on Mondays: Mandfar and Masimba **8 February**; Persimmon and ProPlastics **15 February**; Rhopower and The Grain Hub **22 February**; Trends **1 March**. Review on Friday 5 March
4. South Africa provisional	8–19 Mar 2027	W17–W18	Enviro Plastic, Mangethe, Thando Kinetics	Rand exchange rate and South African supplier document rules prepared during the third wave. Set up and train 8 to 12 March. **Live Monday 15 March**, confirmed at the 5 March review

The festive period, 21 December to 1 January. The pilot falls across it on purpose: the units buy less, so a problem found then costs little, and the two live weeks before it already produce real purchases. During the break nothing new is set up, nobody else goes live, and the technical team is reachable by telephone. The pilot's third full week of purchasing is 4 to 8 January, and the exit tests count everything from 7 December.

> **Fallback.** Each unit keeps its old process available for one month after its go-live, for that unit alone. Purchases already under way when it goes live finish in the old process; new requisitions are raised only in Procureline. The pilot units close their fallback at the go decision on 15 January.

4.2 One week of set-up, for every unit

The same week for every unit, pilot or wave. The unit's administrator coordinates; the owner column says who does each day. The steps are the launch checklist in the Launch Manual, 1.3.

DAY	TASK	OWNER
Monday	Create the unit's administrator; sites and departments, each with its head and deputy; users, one per role, each with a real email address	Technical team, unit administrator
Tuesday	**Confirm the approval limit and the approval chain against the unit's own delegation of authority.** Set the exchange rate for a rand unit	Finance, COO
Wednesday	Suppliers: create or import, complete their documents, submit for activation and approve. Load the item catalogue, opening stock per site and the annual budget per department	Procurement, Head of Procurement, Stores, Finance
Thursday	Training, one session per role, on the unit's own suppliers, items and departments. Invited suppliers register and sign in at least once	Trainers, Procurement
Friday	One rehearsal purchase from requisition to payment, including an order above the limit. Confirm that no other unit's data is visible. **Go or no-go for Monday**	All roles, technical team

A unit whose rehearsal purchase fails on Friday does not go live on Monday. It repeats the failed step the following week and takes the next slot; the other units in its wave keep their dates.

4.3 Pilot exit tests

Assessed in the week of 4 January 2027 with the results in front of the review on 15 January. All six must be true for the second wave to start on 18 January.

#	EXIT TEST	EVIDENCE
1	At least ten real requisitions have reached payment in each pilot unit	Payments list
2	At least one order above the COO limit has passed every approval stage	The order's approval history
3	At least one invoice has been correctly refused for goods not receipted	The rejected invoice and its reason
4	Stock figures agree with a physical count	Inventory against the count sheet
5	Finance confirms the budget figures match its own records	Budgets page
6	No unresolved issue rated urgent	The issue list


The review decides one of three things and writes it down: proceed on 18 January; proceed after named fixes, which moves every later date by the same number of weeks; or stop and revert the pilot units to their old process.

4.4 Main risks

RISK	RESPONSE
The gate is not passed by 27 November	The pilot moves a week for every week lost. Nobody goes live on the test set-up to make up time
Low purchase volumes over the festive period	Two live weeks come before it and one after. If the exit tests are still short on 8 January, the review extends the pilot by two weeks rather than lowering the bar
A unit's approval rules do not fit the default	The limit and chain are set per unit on the Tuesday of its set-up week, before anyone is trained on them
Suppliers do not register	Invitations go out two weeks before each unit's set-up week. Without three suppliers who can quote, the three-quotation control quietly lapses
Two units a week proves too fast	A unit that fails its Friday rehearsal takes the next week's slot. The third wave has a spare week (W16) before the review, so it absorbs one slip without moving South Africa
Data loss	Off-site backups and a restore that has been performed and timed, before the pilot starts
South African rules not ready	Phase 4 stays provisional. It is confirmed, moved or re-planned at the 5 March review, and the Zimbabwe dates do not depend on it
Key people on leave in December	Each pilot unit names a deputy for its department heads and its approvers before 4 December; the system lets the administrator assign one in a minute

4.5 Launch schedule

The whole rollout on one page, from Monday 16 November 2026. Each unit spends one week on set-up and training, goes live on the following Monday and stays live. South Africa is provisional until the review on 5 March.

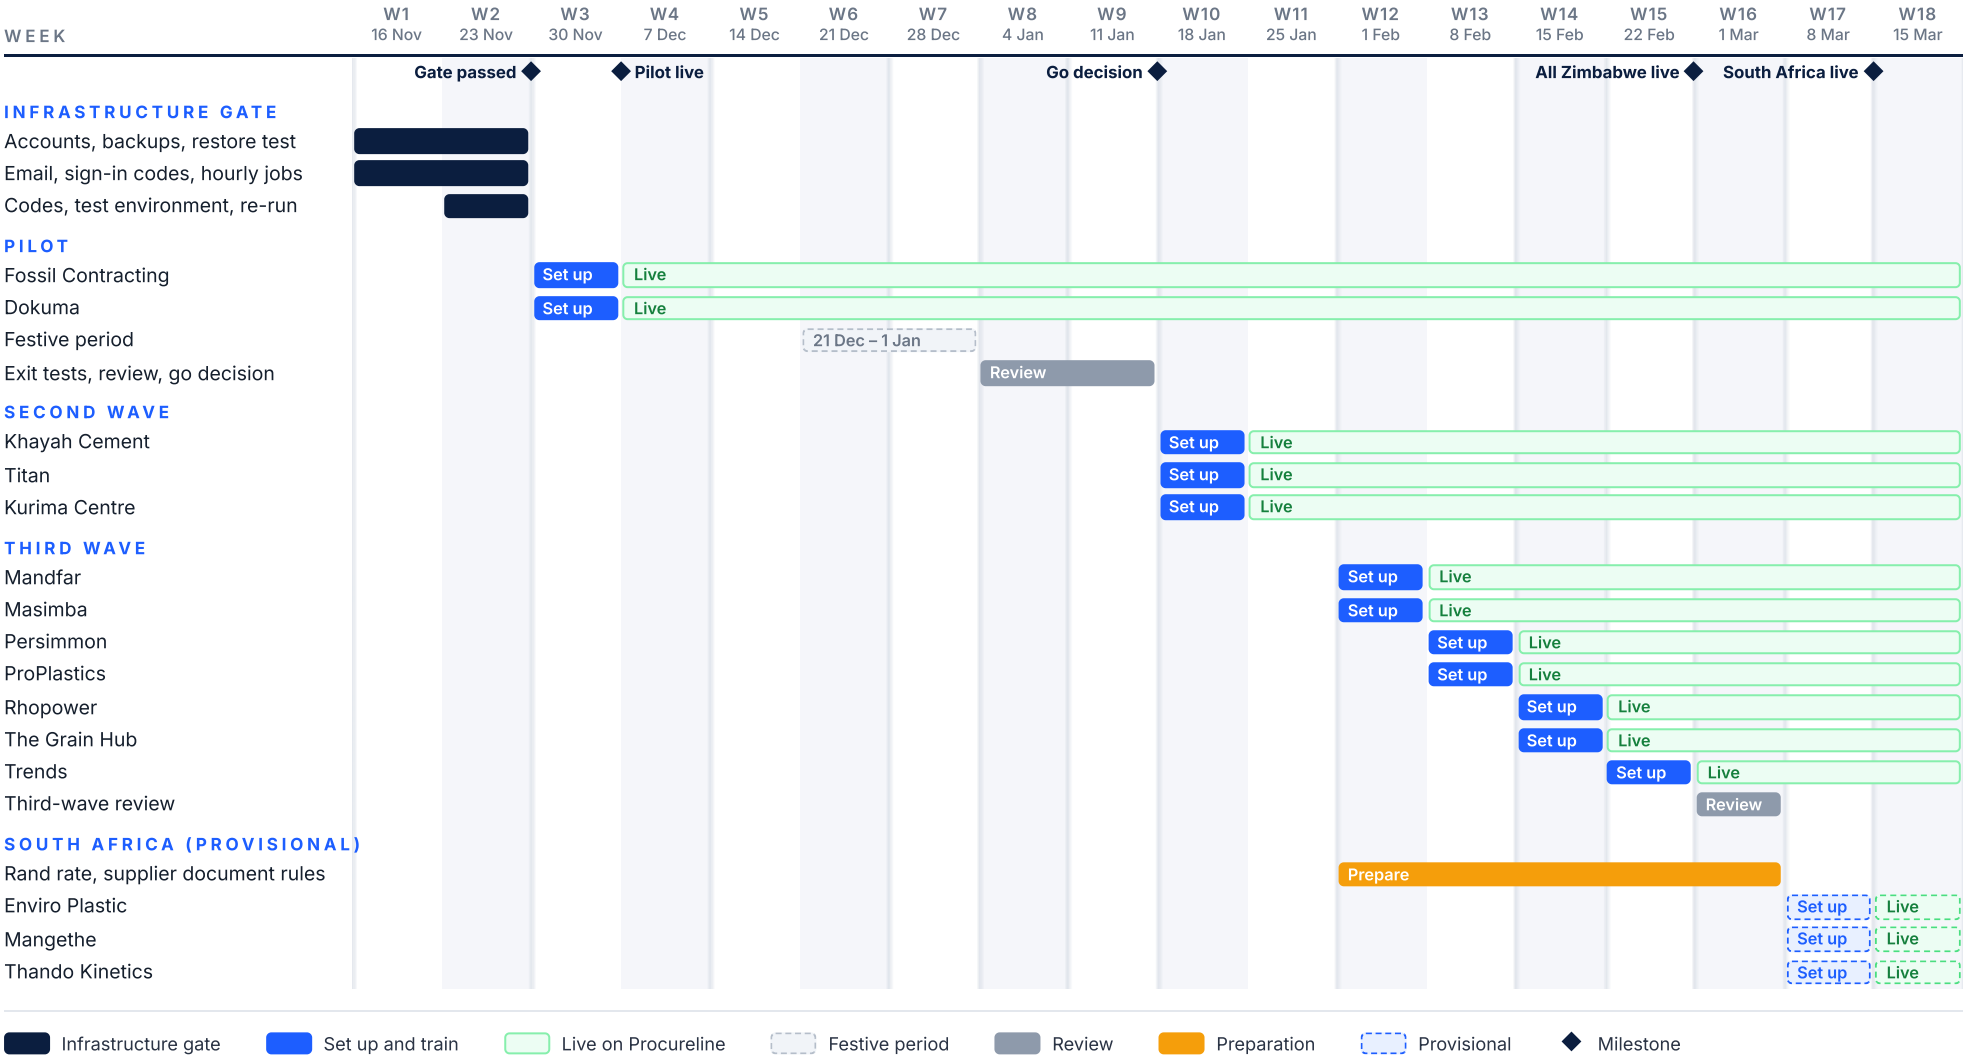

Procureline
PROCUREMENT SYSTEM

Thank you

Questions and comments on this plan go to the rollout lead. The Launch Manual says how each unit is set up; the User Manual says how each role works.

www.procureline.co.zw

WEBSITE	DOCUMENT	VERSION
www.procureline.co.zw	Procureline Rollout Plan	1.0 · 6 November 2026
